

January 27, 2017

Gilbane Construction Update


Activities in progress as of January 27, 2017:

- ▶ Curtain wall framing installation in Area E Cedar Level Reading Area started.
- ▶ Metal stud framing & HVAC installation in Area C Washington Level Scene Shop in progress.
- ▶ Basketball equipment in Area B Washington Level Competition Gym in progress.
- ▶ Painting spiral ductwork in Area C Washington Level Auxiliary Gym in progress.
- ▶ Masonry block fill in Cedar Level Area E in progress.
- ▶ Bay windows installed on 3rd floor Area G Locker Area.
- ▶ Pool stainless steel polishing in progress.
- ▶ Elevators #1, 2 & 3 installation in progress.
- ▶ Corridor quarry tile layout in 2nd floor Area A in progress.
- ▶ Gypsum board installation in 3rd floor Area G coffered ceiling in progress.
- ▶ Interior masonry partition walls in Area A Washington Level in progress.
- ▶ Carpet tile & rubber flooring installation in Areas A, F & G 2nd floor classrooms in progress.

Upcoming Project Milestones:

- ▶ Competition Gym wood flooring installation scheduled to start on 02/06/17.
- ▶ Vocal Level wood flooring installation scheduled to start on 02/02/17.
- ▶ Competition Gym telescoping bleacher installation scheduled to start on 03/17/17.

Construction Key Plan:

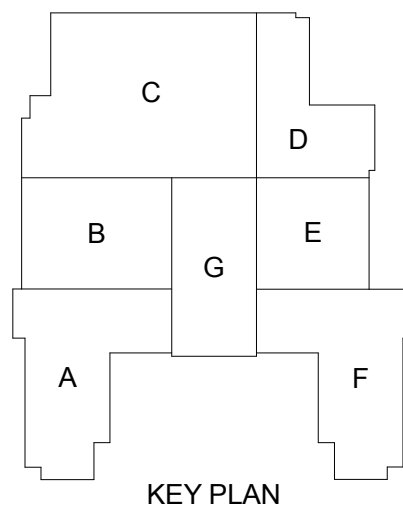



Area A 3rd Floor Atrium



Area F Cedar Level Reading Area



Area G 3rd Floor Locker Area Bay Windows



Area G 2nd Floor Science Hall



Area C Washington Level Scene Shop



Area E Cedar Level Dining Commons

