

March 17, 2017

Gilbane Construction Update


Activities in progress as of March 17, 2017:

- ▶ Ceiling grid installation on Area G 4th floor started.
- ▶ Ceiling framing & drywall laminating on Area A existing stairwell started.
- ▶ Quarry tile installation on Area D Cedar Level Kitchen started.
- ▶ Coffered ceiling diffusers installation on Area G 2nd floor started.
- ▶ Locker installation on Area G 3rd floor started.
- ▶ Rubber wall base installation on Area A 3rd & 2nd floor in progress.
- ▶ Casework installation on Area G 3.5 level, Area G 4th floor & Area A Cedar level in progress.
- ▶ Porcelain floor tile on Area C Washington Level bathrooms in progress.
- ▶ Wood flooring installation on Area G 4th floor in progress.
- ▶ Painting on Area A Washington Level in progress.
- ▶ Painting coffered ceilings on Area G 2nd floor in progress.
- ▶ Drywall installation on Areas C, D & E Cedar Level in progress.
- ▶ Areas A & F canopy structural steel installation in progress.

Upcoming Project Milestones:

- ▶ Competition Gym telescoping bleacher installation scheduled to start on 04/17/17.

Construction Key Plan:

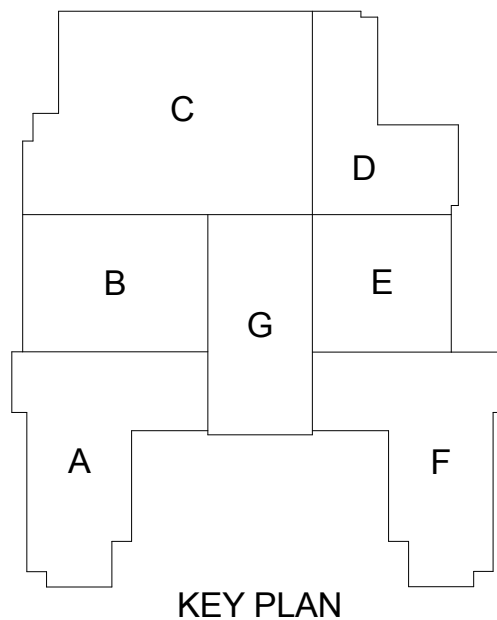



Casework Installation Area C 2nd Floor



Wood Floor Installation Area G 4th Floor



Cauffered Ceiling Installation Area G Cedar Level



Quarry Tile Installation Area D Kitchen



Locker Installation Area G 3rd Floor



Storefront Installation Area E Cedar Level

