

May 06, 2016

Gilbane Construction Update


Activities in progress as of May 06, 2016:

- ▶ Courtyard masonry cleaning & tuck pointing in progress
- ▶ Topping slab for the 3rd floor will be complete today
- ▶ Area D Washington level being prepped for slab on grade
- ▶ Areas A & F 3rd floor ductwork & pipe hangers installation in progress
- ▶ Exterior stud framing in Area A Washington, Cedar & 2nd floor & Area F Cedar & 2nd floor in progress
- ▶ Masonry walls in Areas C & D Washington level in progress
- ▶ Excavation for pool surge tank in Area C Washington level started
- ▶ Area C Washington level Mechanical Room retaining wall reinforcement steel in progress
- ▶ Drilling for geothermal well field started
- ▶ Area B roof decking in progress
- ▶ Area G 4th floor ductwork in progress
- ▶ Area A roof drains in progress

Upcoming Project Milestones:

- ▶ Area D slab on grade pour planned for week of 5/9
- ▶ 2nd floor topping slab planned for week of 5/9

Construction Key Plan:

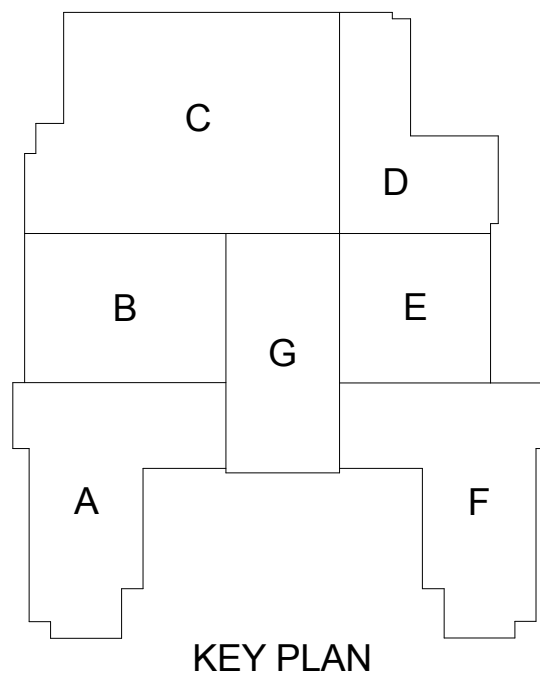




Area A Topping Slab Placement



Area F Exterior Studs



Area C Pool Surge Tank Excavation

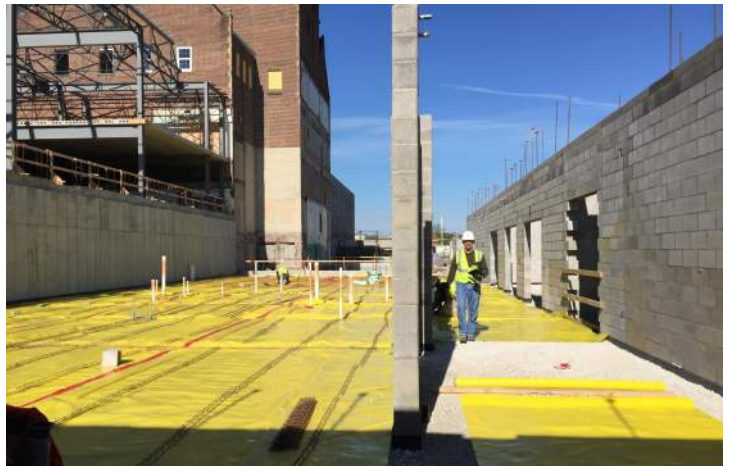

Area D Washington Level Slab-On-Grade Prep



Area C Masonry Walls



Area A Exterior Studs

