

December 09, 2016

Gilbane Construction Update


Activities in progress as of December 09, 2016:

- ▶ Spiral duct painting in Competition Gym on Washington level started.
- ▶ Door openings above Auditorium Stage in progress.
- ▶ Interior painting in Areas A, F & G 2nd & 3rd floor in progress.
- ▶ Drywall installation in Areas B & E 2nd floor in progress.
- ▶ Metal stud framing in Area C 2nd floor in progress.
- ▶ Chauffeured ceiling layout in Area G 2nd floor in progress.
- ▶ Ceiling grid installation in Areas A, F & G 2nd & 3rd floor in progress.
- ▶ Casework installation in Area A 2nd & 3rd floor in progress.
- ▶ Interior masonry in Area D Cedar level Kitchen in progress.
- ▶ Ceiling tile borders, lights, speakers & sprinkler drops on 2nd floor Areas A, F & G in progress.
- ▶ Removal of temporary lighting & installation of permanent lighting in Area A 3rd floor in progress.
- ▶ Metal veneer panels in Area F north elevation in progress.

Upcoming Project Milestones:

- ▶ Finish flooring scheduled to start week of 12/12/16.

Construction Key Plan:

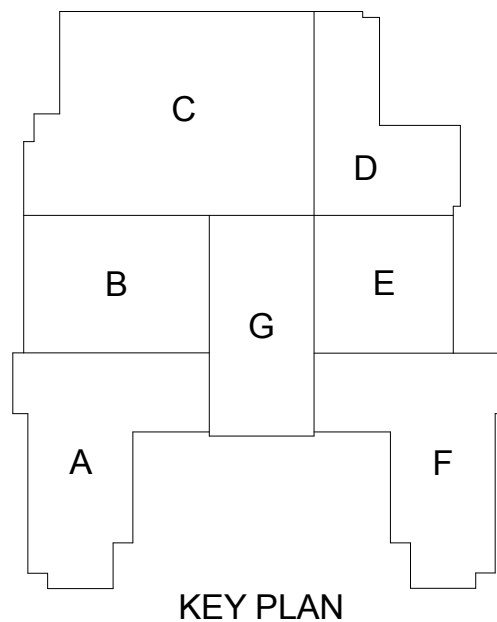



Area A Washington MEP Rough-In



Courtyard View



Area F Cedar Level Mini Auditorium Framing



Area A 3rd Floor Casework Installation



Area A 2nd Floor Ceiling, Lights, Speaker & Sprinkler Installation



Competition Gym Spiral Duct Painting

