

July 22, 2016

Gilbane Construction Update


Activities in progress as of July 22, 2016:

- ▶ Spray foam on Area F east elevation & Areas A & B west elevation in progress
- ▶ Existing courtyard window demo & installation of new window mullions in progress
- ▶ Masonry veneer in Area A west elevation started
- ▶ Interior masonry in Areas B & E Cedar Level in progress
- ▶ Slab-on-grade in Areas D & B Cedar Level poured
- ▶ Roof bar joists in Area D installation in progress
- ▶ Electrical underground ductbank installation from transformer to main electrical room in progress
- ▶ Roof decking installation in Area E in progress
- ▶ Auditorium demolition in progress
- ▶ Electrical in-wall rough-in on Cedar & 2nd Level Areas A, F & G in progress
- ▶ Interior stud wall framing on Cedar, 2nd & 3rd Level Areas A, F & G in progress
- ▶ Hollow core in Areas C & D Cedar Level set
- ▶ HVAC duct & piping 2nd & 3rd Level Areas A, F & G & 4th Floor Area G in progress
- ▶ Electrical overhead rough-in on 3rd & 2nd Level Areas A, F & G in progress
- ▶ Domestic piping & sanitary installation on 2nd & 3rd Level Areas A, F & G in progress
- ▶ Spray-on-fireproofing in progress
- ▶ Interior bathroom masonry in Area F 2nd Floor in progress
- ▶ Cable tray installation in Areas A & F 3rd Floor in progress
- ▶ Area A south stairs poured
- ▶ Clock tower restoration in progress

Upcoming Project Milestones:

- ▶ Air handling units #1 & #2 installation start 8/1
- ▶ Glazing Area A to start 8/8
- ▶ Drywall on 3rd Level to start 8/8

Construction Key Plan:

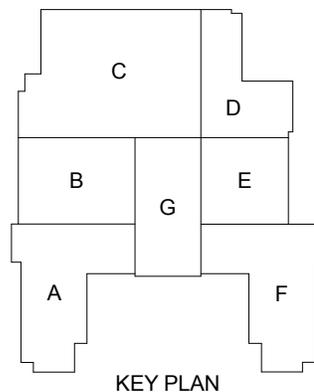



Area A Spray Foam & Masonry Veneer



Area F Spray Foam & Masonry Veneer



Area C Cedar Level Hollow Core



Area C Cedar Level Interior Masonry



Courtyard Existing Window Demo



Clocktower Restoration

