

July 29, 2016

## Gilbane Construction Update


### Activities in progress as of July 29, 2016:

- ▶ Area A Washington Level prep for slab-on-grade pour
- ▶ Area B Washington Level Competition Gym prep for slab-on-grade pour
- ▶ Spray foam on Area F east elevation & Areas A & B west elevation in progress
- ▶ Existing courtyard window demo & installation of new window mullions in progress
- ▶ Masonry veneer in Area A west elevation in progress
- ▶ Interior masonry in Areas B & E Cedar Level in progress
- ▶ Roof decking in Area D installation in progress
- ▶ Roof decking installation in Area E in progress
- ▶ Auditorium demolition in progress
- ▶ Electrical in-wall rough-in on Cedar & 2<sup>nd</sup> Level Areas A, F & G in progress
- ▶ Interior stud wall framing on Cedar, 2<sup>nd</sup> & 3<sup>rd</sup> Level Areas A, F & G in progress
- ▶ HVAC duct & piping 2<sup>nd</sup> & 3<sup>rd</sup> Level Areas A, F & G & 4<sup>th</sup> Floor Area G in progress
- ▶ Electrical overhead rough-in on 3<sup>rd</sup> & 2<sup>nd</sup> Level Areas A, F & G in progress
- ▶ Domestic piping & sanitary installation on 2<sup>nd</sup> & 3<sup>rd</sup> Level Areas A, F & G in progress
- ▶ Spray-on-fireproofing in progress
- ▶ Interior bathroom masonry in Area F 2<sup>nd</sup> Floor in progress

### Upcoming Project Milestones:

- ▶ Air handling units #1 & #2 installation start 8/1
- ▶ Glazing Area A to start 8/8
- ▶ Drywall on 3<sup>rd</sup> Level to start 8/8

### Construction Key Plan:

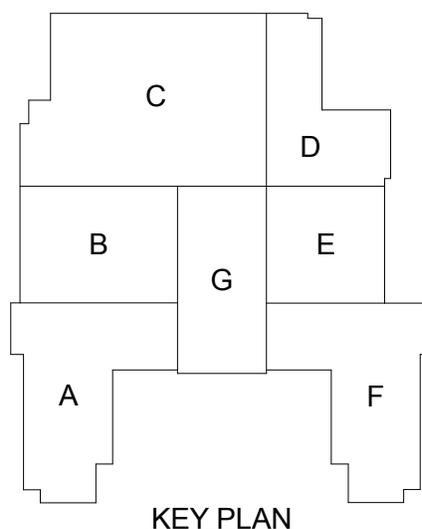



Area A West & South Elevation Brick Veneer



Area B Competition Gym Prep for Slab-On-Grade



Area F Cedar Level Plumbing & Framing



Area F West Elevation Spray Foam



Area C Cedar Level Interior Masonry



Area D Roof Decking

