Volume No. 99

July 27, 2017

## Gilbane Construction Update


## Activities in progress as of July 27, 2017:

- District deliveries in progress
- Installation of memorial items in progress
- Carpet instillation in Cedar level north corridor in progress
- Installation of furniture in Dinning Commons in progress
- ▶ Life safety testing in progress
- Display case installation in progress
- ▶ Installation of auditorium equipment in progress
- ▶ Repair of drywall throughout building in progress
- Cleaning exterior of the building in progress
- Owner training in progress
- Final cleaning of the interior of the building in progress
- ▶ Furniture installation in Dinning Commons in progress

## **Upcoming Project Milestones:**

- ▶ August 1<sup>st</sup>: Gilbane turns over building
- ▶ August 1<sup>st</sup>: Obtain certificate of occupancy

## **Construction Key Plan:**

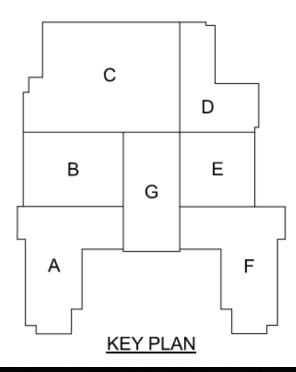







Cedar Level North Corridor Carpet



**Dinning Commons Furniture** 



**District Delivery** 



**Display Cases** 



**Auditorium Equipment** 



Wall Repairs Throughout Building

