

April 07, 2017

## Gilbane Construction Update


### Activities in progress as of April 07, 2017:

- ▶ Wood flooring installation in Area C Auxiliary Gym started.
- ▶ Prep for quarry tile installation in Area D Kitchen walk-in coolers started.
- ▶ Painting in Area G Auditorium balcony & Area F south stairwell started.
- ▶ Drywall installation & existing plaster restoration in Auditorium in progress.
- ▶ Stage theatrical equipment installation in Auditorium in progress.
- ▶ Metal lockers installation on 2<sup>nd</sup> floor Area G in progress.
- ▶ Carpet tile installation on 2<sup>nd</sup> floor Area G corridors in progress.
- ▶ Lighting installation on 4<sup>th</sup> floor Area G in progress.
- ▶ Casework installation on 4<sup>th</sup> floor Area G in progress.
- ▶ Courtyard grading & site topsoil placement in progress.

### Upcoming Project Milestones:

- ▶ Competition Gym telescoping bleacher installation scheduled to start on 04/17/17.
- ▶ Kitchen equipment delivery scheduled for 04/17/17.

### Construction Key Plan:

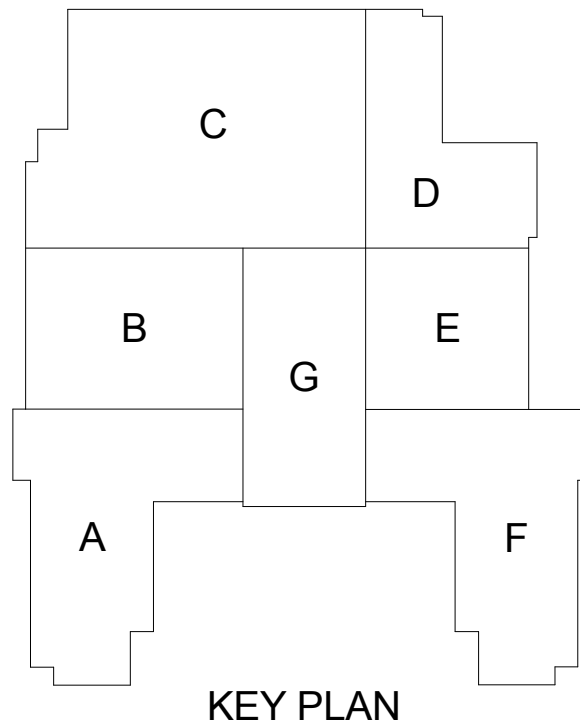



Carpet Installation in 2nd Floor Area A Corridor



Drywall Installation & Plaster Repair in Auditorium



Casework Installation on 4th Floor Area G



Wood Flooring Installation in Auxiliary Gym



Wood Flooring Installation on 4th Floor Area G



Metal Stair Painting Area F South Stair

